


Generator Interconnection Process


DPP Phase 1 + DPP Phase 2 + DPP Phase 3 + GIA = ~ 373 Days

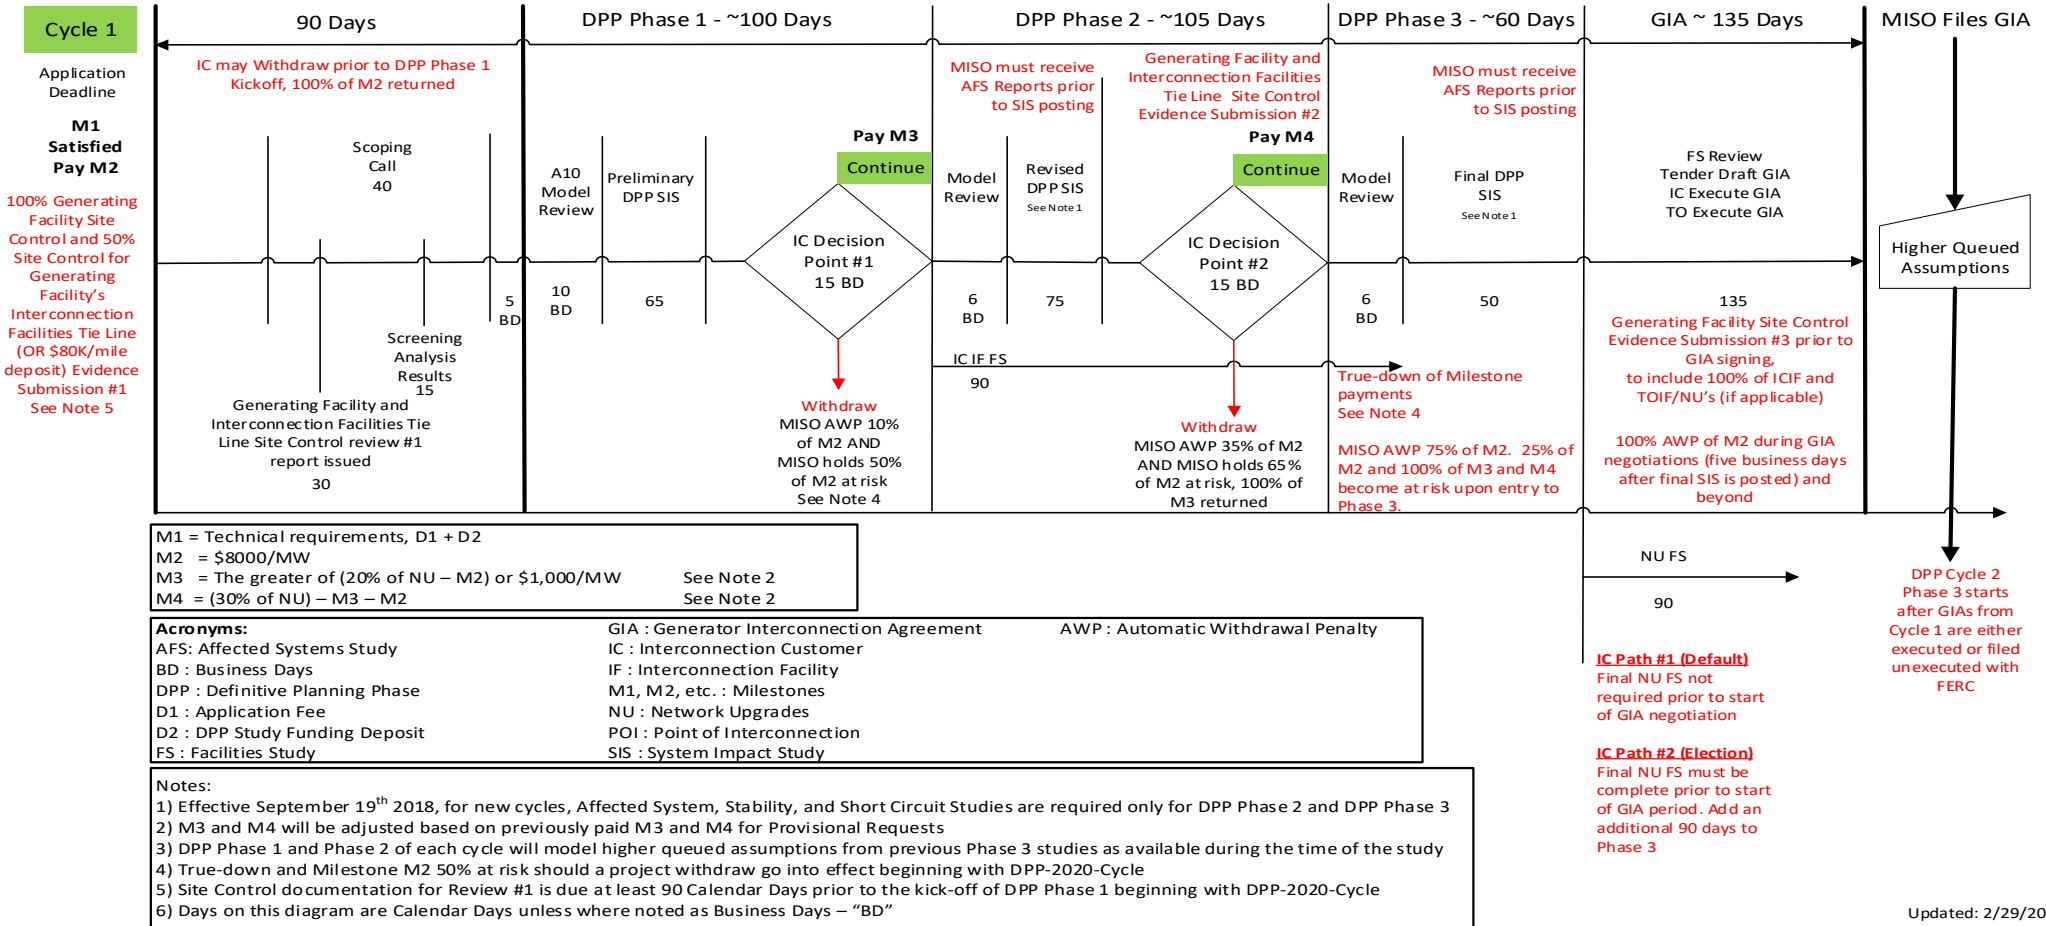

Updated: 2/29/2024

Generator Interconnection Process

DPP Phase 1 + DPP Phase 2 + DPP Phase 3 + GIA = ~ 373 Days

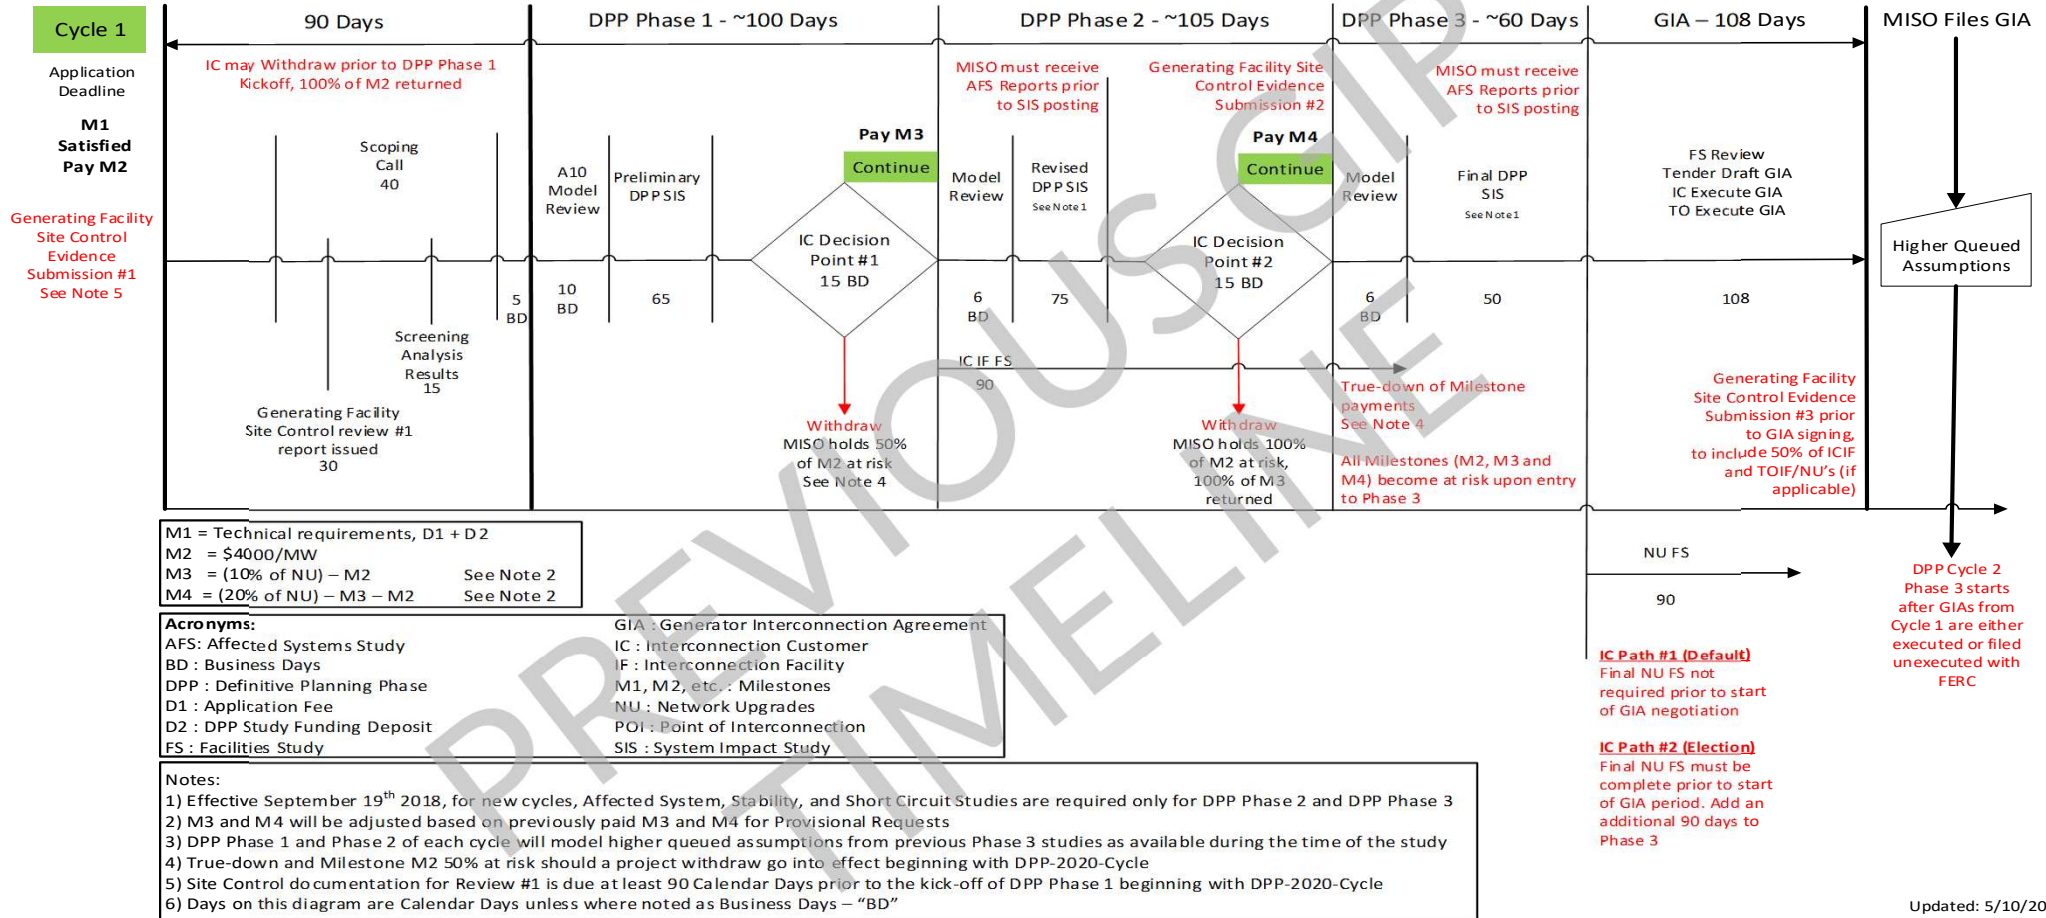

Updated: 5/10/2022

GIP Timeline Reduction Overview

DPP I → GIA	Previous Timeline	NEW Timeline		Timeline Duration Change	
		Path #1	Path #2	Path #1	Path #2
DPP I	~140 Calendar Days	~100 Calendar Days		↓ ~40 Calendar Days	
DPP II	~80 Calendar Days	~105 Calendar Days		↑ ~25 Calendar Days	
DPP III	~135 Calendar Days (90 Day NUFS Included)	~60 Calendar Days (NUFS <u>Not</u> Required)	~150 Calendar Days (NUFS Required)	↓ ~75 Calendar Days	↑ ~15 Calendar Days
GIA	~150 Calendar Days	~108 Calendar Days	~108 Calendar Days	↓ ~42 Calendar Days	
Totals	~505 Calendar Days	~373 Calendar Days	~463 Calendar Days	↓ ~132 Calendar Days	↓ ~42 Calendar Days

GIP Timeline Reduction - Path #1 vs Path #2

